

ARCHITECTS LAWAL SCOTT ERICKSON ARCHITECTS, INC.

www.lse-architects.com

These drawings including all design, details, specifications and information, are the sole copyright of LSE Architects, Inc. and are for use on this specific project and shall not be used on any other work without agreement and written permission of LSE Architects, Inc. ©

WILLMAR REC/ **EVENTS CENTER** SCHEMATIC

ANDERSON - JOHNSON ASSOCIATES, INC.

A (1) BOLTON & MENK COMPANY

I hereby certify that this plan, specification, or report was prepared by me or under my direct supervision, and that I am a duly Licensed Paolessapea A Edigieeter under the laws of the State of Minnesota.

12.18.20 DD Set

Copyright © LSE Architects, Inc.

ARCHITECTS

LAWAL SCOTT ERICKSON ARCHITECTS, INC.

100 Portland Ave. South, Suite 100 Minneapolis, MN 55401


612.343.1010 office 612.3382280 fax

Www.lse-crchitects.com

These drawings including all design, details, specifications and information, are the sole copyright of LSE Architects, Inc. and are for use on this specific project and shall not be used on any other work without agreement and written permission of LSE Architects, Inc. ©

CITY OF
WILLMAR EVENT
AND
RECREATION
CENTER

2707 Arena Drive Willmar, MN 56201

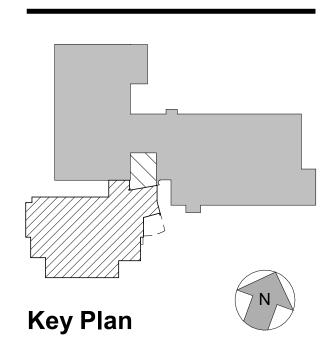



No.	Date	Revision Description				
	04.30.20	SCHEMATIC DESIGN				
	12.18.20	DESIGN DEVELOPM				
		-				
		-				
	-	_				
		-				
		-				
	_	-				
		-				
DECICAL DEVEL OBMENT						
DESIGN DEVELOPMENT						

ADDITION FLOOR PLAN

 Project
 19.1030.01
 Drawing Num

 Date
 12.18.20

 Drawn by
 MM / CL

1 ADDITION A210 1/8" = 1'-0"

Copyright © LSE Architects, Inc.



ARCHITECTS

19.1030.01 Drawing Number

Copyright © LSE Architects, Inc.



Entry Rendering
Design Development Review | January 27, 2021



Rendering
Design Development Review | January 27, 2020


Willmar Recreation & Events Center
City of Willmar | LSE Architects

Budget

Construction Budget		\$10,000,000
Marcus Construction Estimate		\$9,943,800
General Conditions (Including Design Fees, CM Fees & Permits) Site Work Concrete Works Masonry Metals Wood & Plastic Insulation Doors & Windows Finishes Special Devices (Toilet Accessories, Folding Partitions, Etc.) Equipment (Basketball Hoops) Furnishings (Bleachers, Walk off Mats, Bike Racks) Mechanical Electrical	\$2,619,317 \$783,765 \$1,087,476 \$414,230 \$844,262 \$12,800 \$721,381 \$543,972 \$581,482 \$324,226 \$89,130 \$46,055 \$1,178,650 \$697,000	
Alternate #02 - Community Room		\$200,000
Potential VE Items (Not including additional alternates)		(\$279,380)
Project Estimate		\$9,864,420



Entry Rendering - Alternate Facade
Design Development Plan Review | January 27, 2020

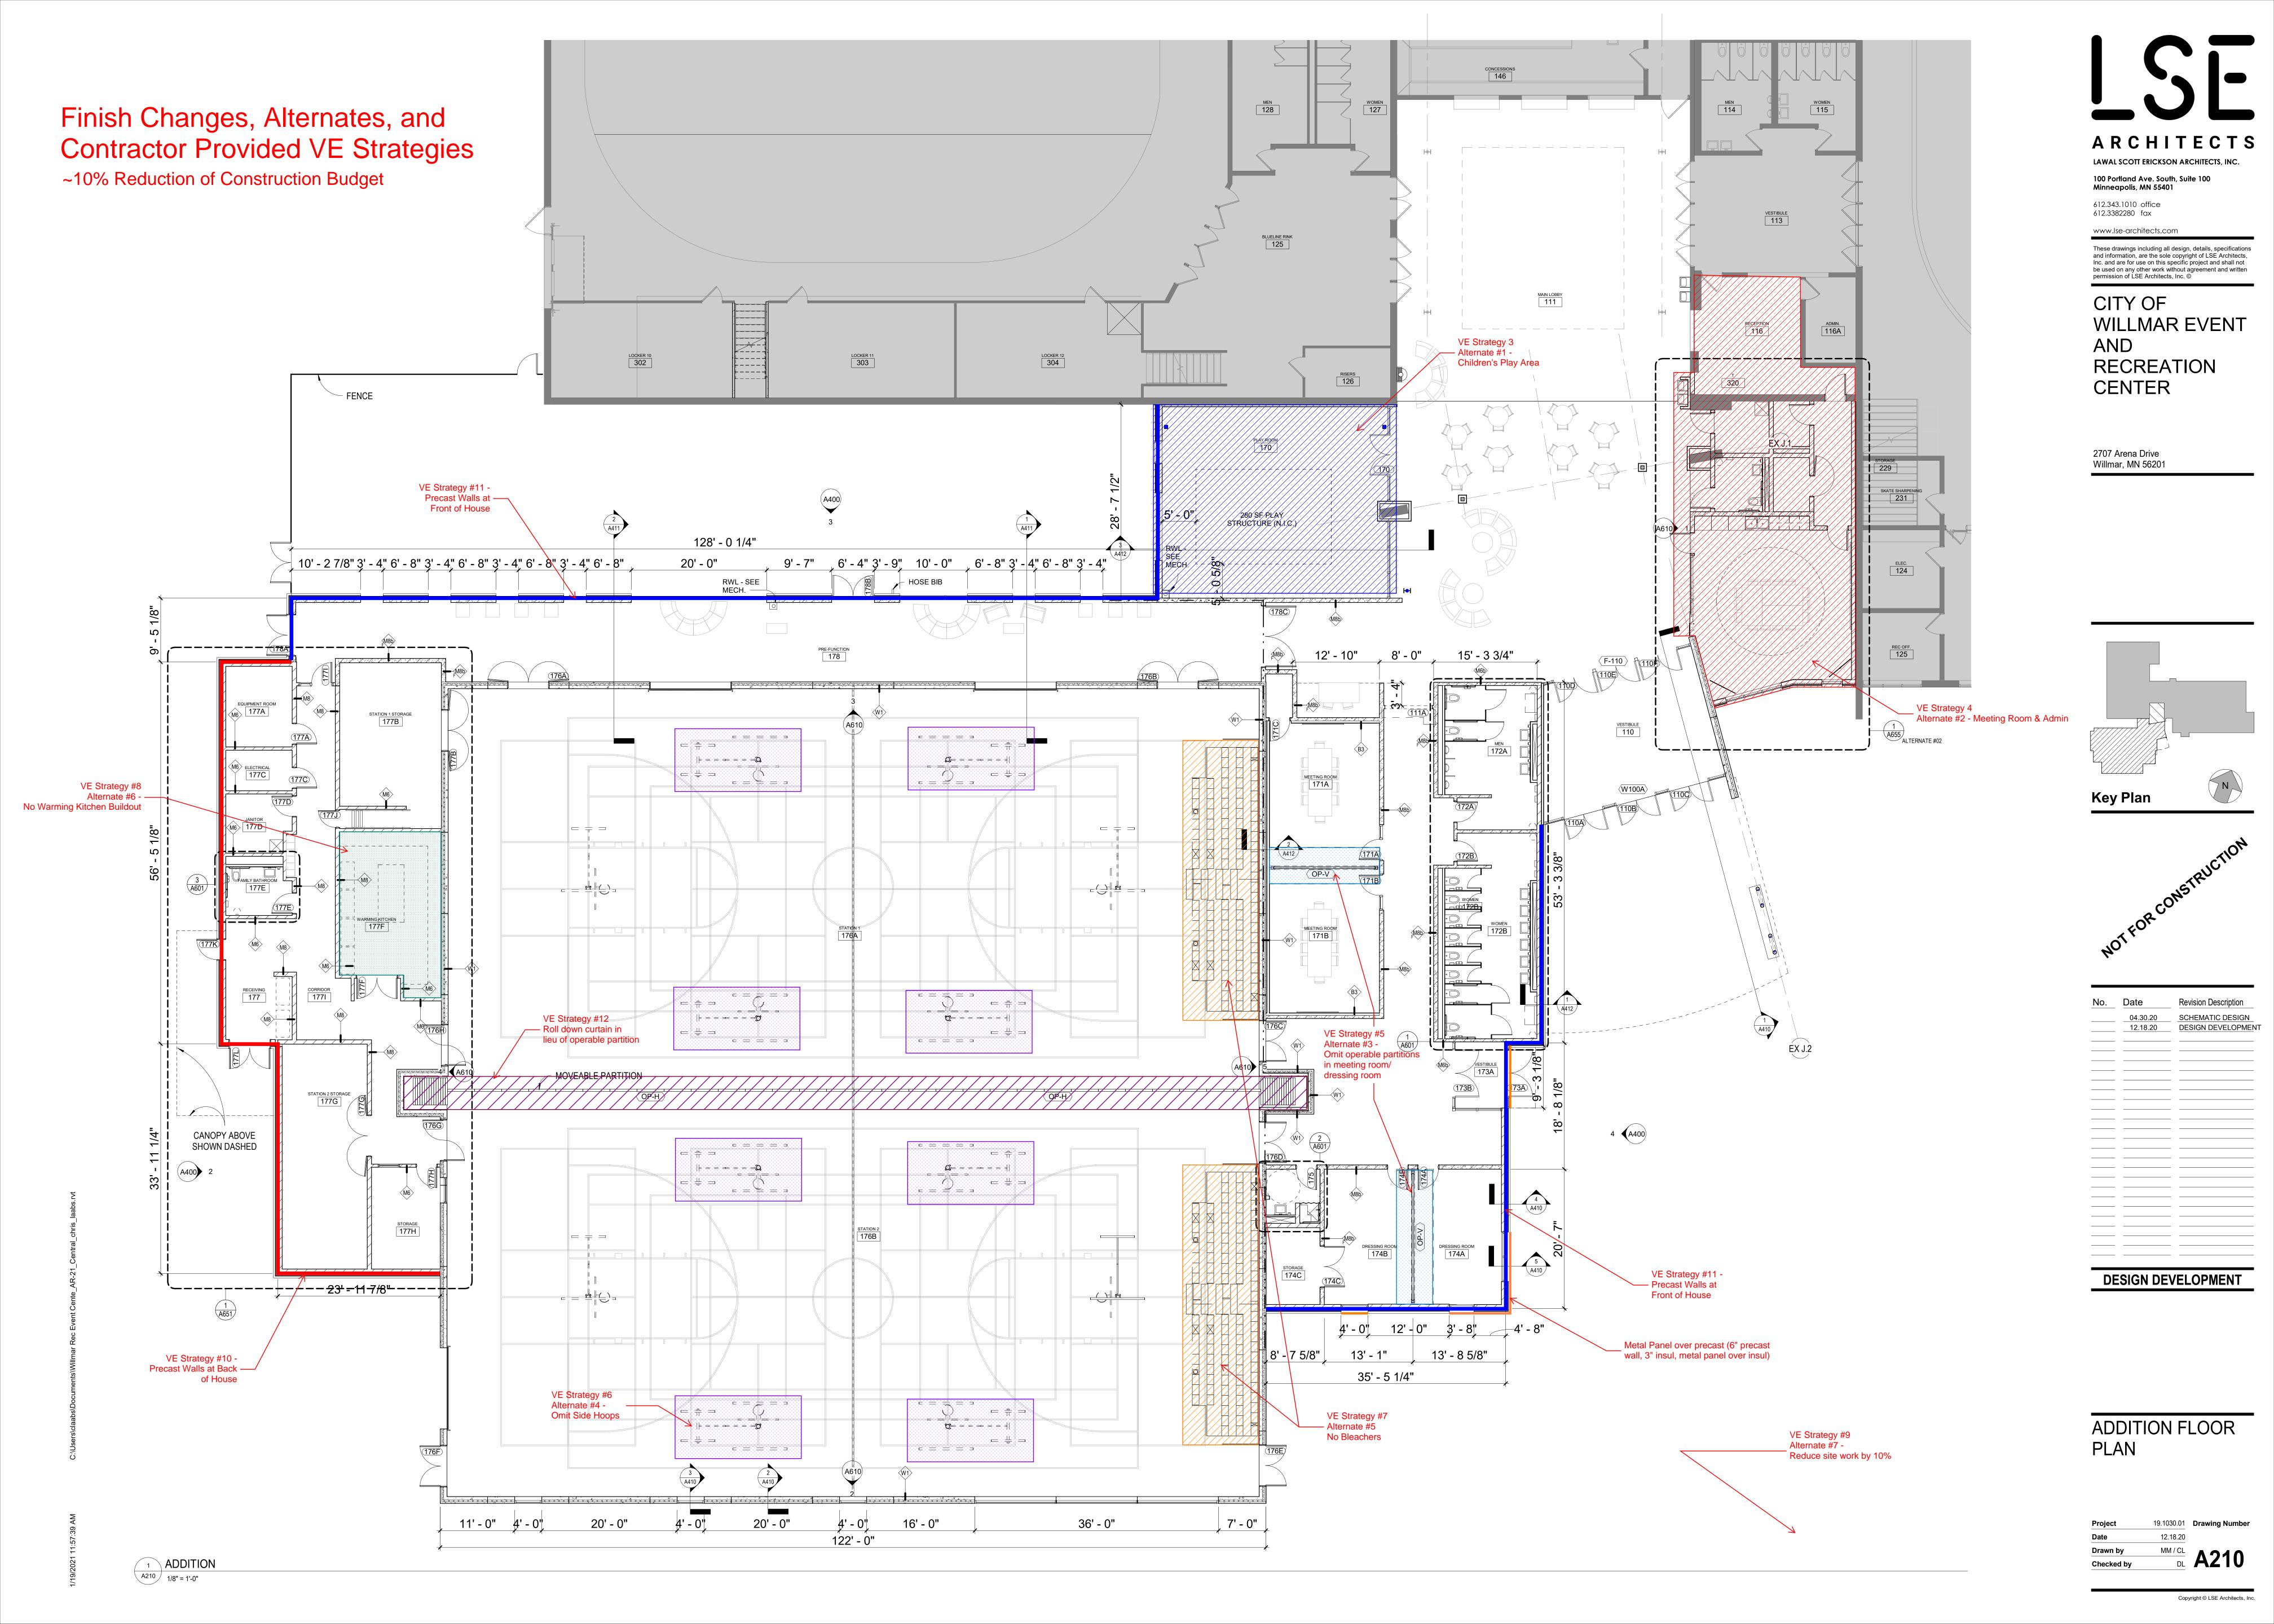

	Strategies		Target Value		Estimated Value	Owner Approval	Comments
Finsh Changes, Alternates, and Contractor Provided VE Strategies (~10% of const. budget)							
1	Finish - Glazed block in lobby only, rest painted CMU	\$	41,000.00	\$	44,000		10% of masonry total
2	Finish - Omit Accoustical Spray at Gym	\$	11,500.00	\$	11,500		per DD pricing
3	Alternate #1 - Children's Play Area	\$	200,968.00	\$	200,000		Estimate from SD Pricing
4	Alternate #2 - Meeting Room / Admin Area	\$	200,000.00	\$	-		Not in base bid, shown as true alternate per DD drawing set
5	Alternate #3 - No operable partitions in meeting rooms	\$	14,692.00	\$	14,692		per DD pricing
6	Alternate #4 - Omit side court basketball hoops (from 12 to 4 hoops)	\$	51,000.00	\$	51,000		per DD budget pricing
7	Alternate # 5 - Bleachers	\$	29,800.00	\$	29,800		per DD pricing
8	Alternate # 6 - No warming kitchen buildout	\$	10,000.00	\$	10,000		per DD budget
9	Alternate #7 - Reduced paving site work	\$	61,076.51	TBD			10% Reduction of paving/sitework
10	Contractor Provided: Precast wall panels in lieu of metal panel over CMU (Back of House)	\$	32,400.00	\$	37,260		135 LF @ \$240 savings per LF of exterior wall
11	Contractor Provided: Precast wall panels in lieu of metal panel over CMU (Front of House)	\$	44,480.00	\$	45,360		278 LF @ \$160 savings per LF of exterior wall (278 LF)
12	Contractor provided: Roll down curtain in lieu of operable partition	\$	150,000.00	\$	165,000		Curtain estimated @ \$20K, added \$15k for possible structural
	Subtotal	\$	846,916.51	\$	608,612		

Project Estimate	\$9,864,420
VE Options	(\$279,380)
Alternates (~6% of Project Cost)	\$567,536.51
Marcus Cost Estimate (Excluding Alternates)	\$9,576,263.49

Key Dates

January 27 - Construction Documents Phase Begins

February 3 - Public Presentation

February 17 - Invest in Willmar Meeting, Public Works & Safety Meeting

March 1 - City Council Approval

March 5 - Construction Documents to Marcus by Noon (End of CD Phase)

March 8 - Bidding Begins

March 30 - Bid Opening
